



Agenda

- Summary of 2017 Pier Demolition Results
 - Dismantling Progress
 - Impact Avoidance Strategy
 - Environmental Monitoring Results
- Next Phase of Project
 - Pier Retention



Our Partners





















THE SAN FRANCISCO-OAKLAND BAY BRIDGE EAST SPAN SEISMIC SAFETY PROJECT

Implosion Permits and Authorizations

- USACE Letters of Modification
- RWQCB SWPPP Amendment Acceptance
- NOAA Marine Mammals Incidental Harassment Authorization
- NOAA Fisheries Biological Opinion
- BCDC Permit Amendments
- CDFW Incidental Take Permit Amendment
- USFWS MBTA Misc. Permit
















SFOBB Dismantling Project Update



LOCATION

Superstructure

• Piers E3 - E5

• Piers E6 - E18

Piers E2, E19-E23

WORK SUMMARY

Removal Completed 2017

Removed in 2015 and 2016

Removed in 2017

Next Phase of Project



Marine Foundation Removal BCDC Permit 2001.008

Amendment No. Forty-one:

- Authorized removal of Piers E4 to E18 via controlled blasting,
- Authorized placement of some demolition debris (28,210 cubic yards) within the footprint of former piers;
- Conditions required minimization measures, monitoring and reporting; and
- Conditions required a presentation to the Commission



Current Status

Status:

- Piers E4 to E18 removed
- Debris removal and site restoration complete
- Piers E4 and E5 briefing to Commission June 1, 2017
- Piers E6 to E18 results report transmitted to BCDC March 28, 2018
- Briefing to Commission April 19, 2018
- Next phase to address remaining piers in process



Summary of 2017 Pier Demolition Results









Key Impact Avoidance and Minimization Strategy

- Seasonal window of implosions (September 1 to November 30)
- Blast attenuation system (BAS)
- Blast plan design
- Bird deterrence
- Robust monitoring program







2017 Implosion Schedule

Blast Event	Pier(s)	2017 Implosion Date	Official Blast Time
1	E7 + E8	September 2	10:36 a.m.
2	E6	September 16	10:00 a.m.
3	E9 + E10	September 30	9:23 a.m.
4	E11 + E12 + E13	October 14	8:51 a.m.
5	E14 + E15 + E16	October 28	7:49 a.m.
6	E17 + E18	November 11	7:27 a.m.



Pier Removal Process

- Above water portions mechanically removed
 - Wire-saw cutting,hoe-ram
- Drilling and loading of charges
- Implosion of underwater portions






Blast Event Video







Post Blast Clean-Up

- Rubble removed to debris removal limit.
- Clean-up verified with bathymetry surveys
- Completed by November 30, 2017
- ~28,210 cubic yards authorized for in-situ (E4 to E18)
- ~24,180 cubic yards placed in-situ (E4 to E18)

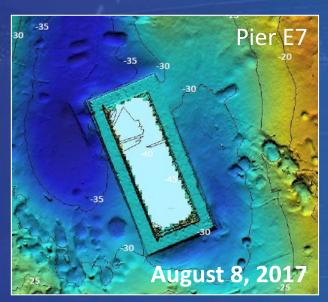

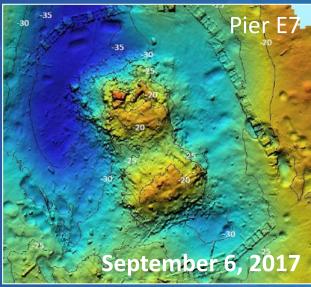

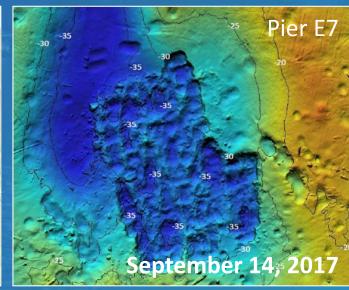



Monitoring Efforts

- Hydroacoustic Monitoring
- Avian Monitoring/Bird Predation Monitoring
- Fish Monitoring
- Marine Mammal Monitoring
- Water Quality Monitoring







Fisheries Monitoring

- Fish Salvage No FESA, CESA fish collected
- Hydroacoustic Monitoring
- Fish Assemblage Survey





Fish Salvage

- Four boats: 2 outside debris boom; 2 inside debris boom
- Fish collected after each blast range 3 to 777 individuals (973 total cumulative)
 - Pier E6 outlier (629 anchovies collected)
 - Most prevalent species were brown rockfish and surfperch (excluding northern anchovy)
 - No FESA- or CESA-listed species observed or collected





Hydroacoustic Monitoring

- Near-field
 monitoring all 6
 controlled blast
 events within 1,100
 feet
- Far-field monitoring on 4 of 6 controlled blast events from 1,500 to 6,000 feet




Example monitoring array (Piers E11-E13)



Hydroacoustic Monitoring

Example Sound Pressure Signatures at 500 feet (Piers E11-E13)
Half second between pier implosions

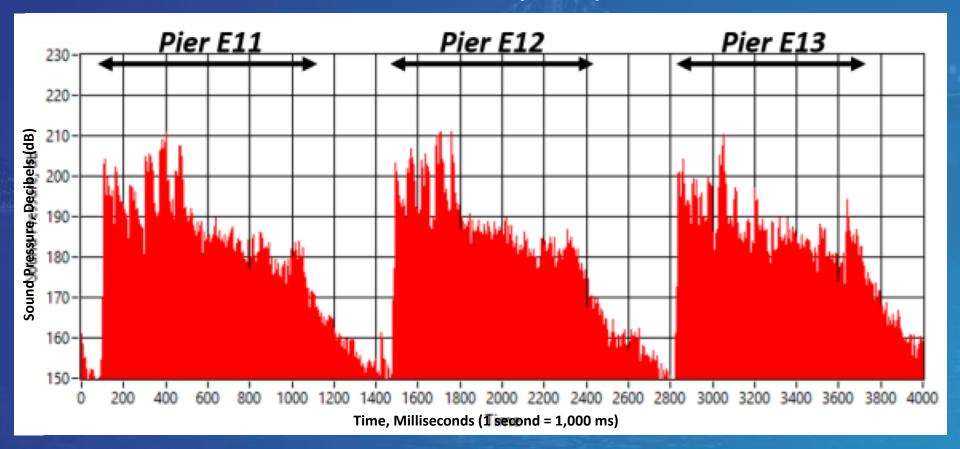



Hydroacoustic Monitoring Results to Fish Criteria

	Distance to Criteria/Threshold					
Piers	Peak	cSEL, ≥ 2 grams	cSEL, < 2			
Piers	Pressure		grams			
	206 dB (feet)	187 dB (feet)	183 dB (feet)			
PERMIT LIMIT	1,165	889	1,230			
E7, E8	312	334	450			
E6	320	312	421			
E9, E10	687	635	858			
E11, E12, E13	730	839	1,132			
E14, E15, E16	650	711	960			
E17, E18	461	339	457			



Fish Assemblage Survey

- Pre-Blast Sonar
 - Two sonar passes were made at approx. 500 and 750 feet around each pier approximately 4 hours prior to each event.
 - Very few areas of fish assemblages were noted in survey areas
 - Correlation difficult to see when compared to post-blast salvage





Avian Monitoring

- Monitored 30 min prior to blasts; bird strike counts were performed post-blast
- Sound cannons flushed birds prior to blasts. Drone used when cannons were ineffective
- No take of avian species occurred

Bird predation (bird strikes) was considered low for all

implosions





Marine Mammals Monitoring

- A minimum of 10 NOAA-approved observers at each blast event
- Marine Mammal Center stranding team on site
 - Stranding surveys conducted for 3-days after each blast event







Marine Mammal Monitoring Results

- Level A vs Level B
- No animals in exclusion zones during blasts
- No stranded animals observed
- No permanent injury authorized or observed

			Count by Species				
Parameter		Harbor Seal	Sea Lion	Elephant Seal	Harbor Porpoise	Bottlenose Dolphin	Northern Fur Seal
Authorized Level B Take: Behavioral		66	18	6	18	6	6
Authorized Level B Take: TTS		48	12	3	9	3	3
2017 Events	Actual Level B Take: Behavioral	9	0	0	0	0	0
	Actual Level B Take: TTS	19	0	0	3	0	0



Water Quality & Sediment Monitoring

- 2017 Monitoring Methods:
 - Fixed buoy monitoring
 - Barge mounted sondes
 - Dynamic plume mapping
 - Static plume tracking
 - Eelgrass ESA monitoring
 - Sediment Assessment





Water Quality & Sediment Monitoring

- Slightly elevated pH
 - To background levels (3.5 hrs)
- Elevated turbidity
 - To background levels (3.5 hrs)
- Eelgrass monitoring:
 - No changes from background
- Sediment:
 - Metals consistent with Regional Monitoring Program









2017 Pier E3 Infill Monitoring

 Net gain in sediment from 2015 to 2017 of 2,840 cubic yards

Dec 2015

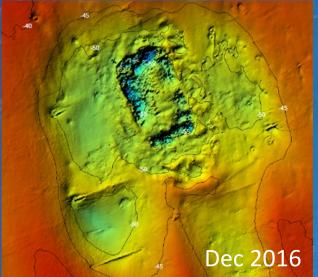

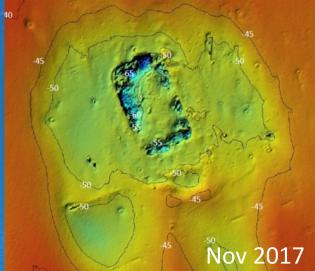

Chromatic scale shows relative depth and depth in feet below 0 feet NGVD29 (red is shallower, blue is deeper)




-25.00

-49.00

-61 00

-73.00

THE SAN FRANCISCO-OAKLAND BAY BRIDGE EAST SPAN SEISMIC SAFETY PROJECT

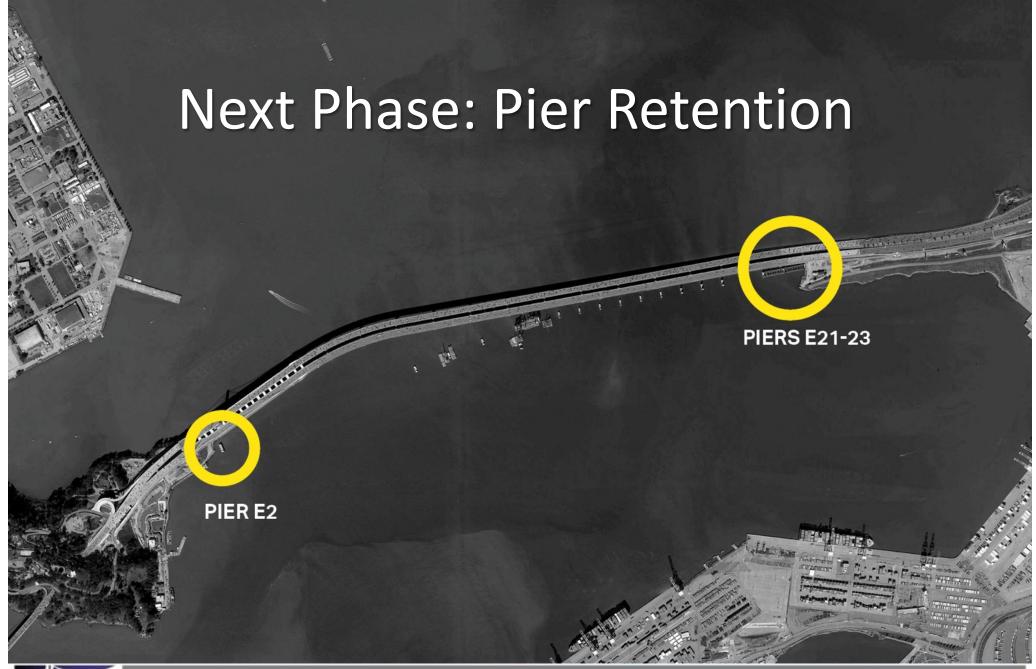



THE SAN FRANCISCO-OAKLAND BAY BRIDGE EAST SPAN SEISMIC SAFETY PROJECT

Overview of Pier Retention Phase

Pier Retention:

YBI (New Structure to Pier E2)

Oakland Touchdown (New Structure on Piers E21-E23)

Demolition (Piers E19-E20)







Pier E2 Public Access Concept





Piers E21 - E23 Public Access Concept








THE SAN FRANCISCO-OAKLAND BAY BRIDGE EAST SPAN SEISMIC SAFETY PROJECT

Pier Demolition – E19/E20

- Demolition using controlled implosions
 - Above water mechanical demolition
 - Below water implosion/ rubble removal
 - Monitoring resources following protocol implemented during 2017 blast events

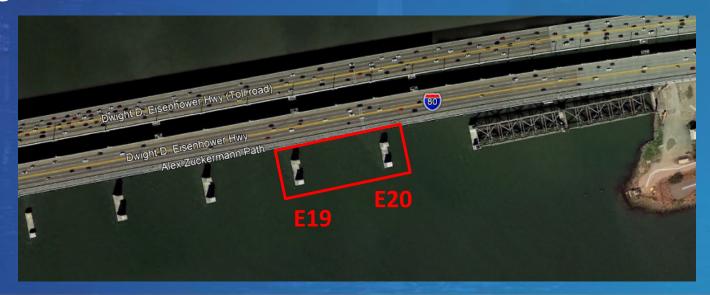



Thank You





THE SAN FRANCISCO-OAKLAND BAY BRIDGE EAST SPAN SEISMIC SAFETY PROJECT
